



City-Owned Arterial
Streetlight
LED Conversion Report #3



October 3, 2023

Project Status Overview

The Works Phase LED Conversion of City-owned arterial roadway streetlights installation continued the past two weeks spanning Monday, 09/18/23, to Friday, 09/29/23. In this two-week period, 283 luminaires were installed.

In total, 868 luminaires have been installed which is 72% of the project scope.

The past two weeks, Dalkia continued work in Segment Two along Northern Blvd. A total of 231 luminaires have been installed in Segment Two.

In Segment Four, Dalkia worked along Broadmoor Blvd, Loma Colorado Dr, and Northern Blvd. A total of 211 luminaires have been installed in Segment Four.

In Segment Five, Dalkia worked along Cabezon Blvd, Sara Rd, Southern Blvd, Broadmoor Blvd, High Resort Blvd, and Country Club Dr. A total of 68 luminaires have been installed in Segment Five.

Sixteen shields have been installed on converted lights, per constituent requests.

Looking ahead, Dalkia will continue to work in Segment One and Two to complete the traffic signal luminaires, as well as in Segment Three along Highway 528.

Conversion Work Completed from 08/21/23 – 09/29/23

PROGRESS TO DATE


Total Complete: 868 luminaires (72% complete)

- Segment 1: 347 luminaires (88% complete)*
- Segment 2: 231 luminaires (86% complete)*
- Segment 3: 11 luminaires (6% complete)*
- Segment 4: 211 luminaires (82% complete)*
- Segment 5: 68 luminaires (70% complete)*

The maps on the following pages show Segment level progress between August 21, 2023 and September 29, 2023.

October 3, 2023

Segment One Progress Map

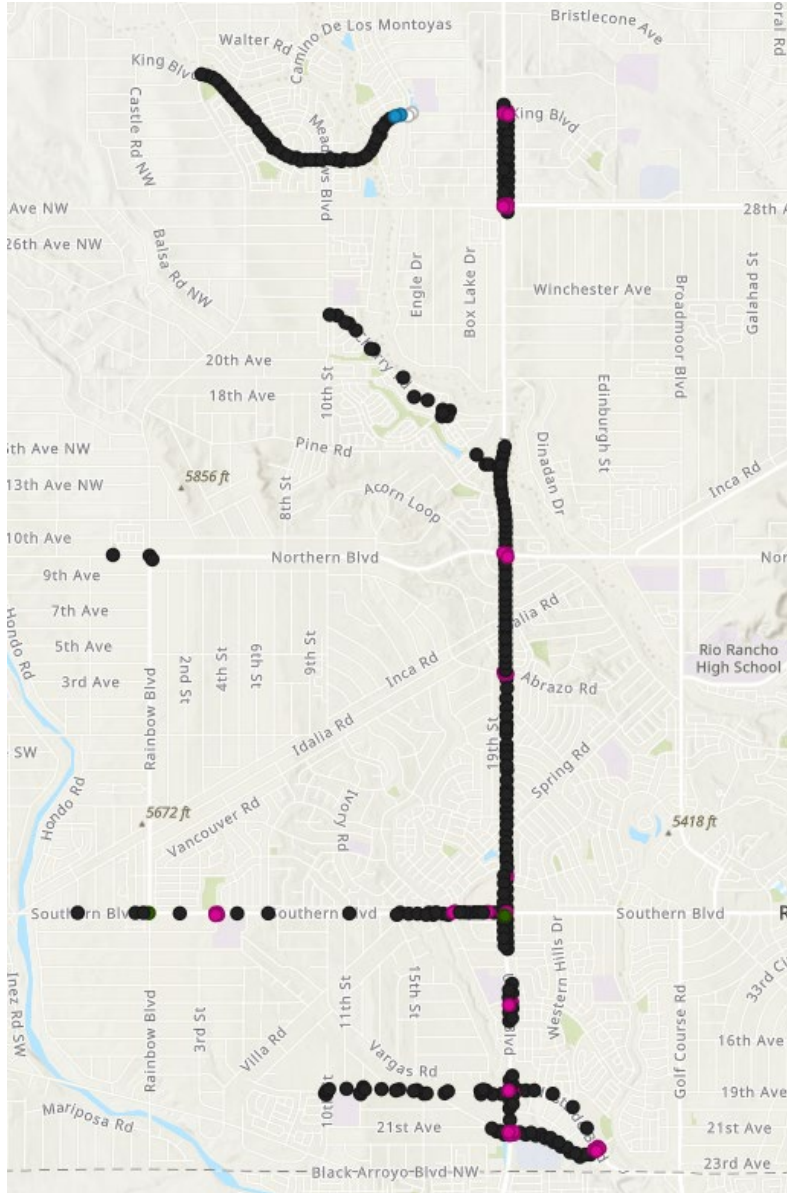


LEGEND

BLACK: Upgrade Complete
ALL OTHER COLORS: Scheduled for Upgrade

October 3, 2023

Segment Two Progress Map

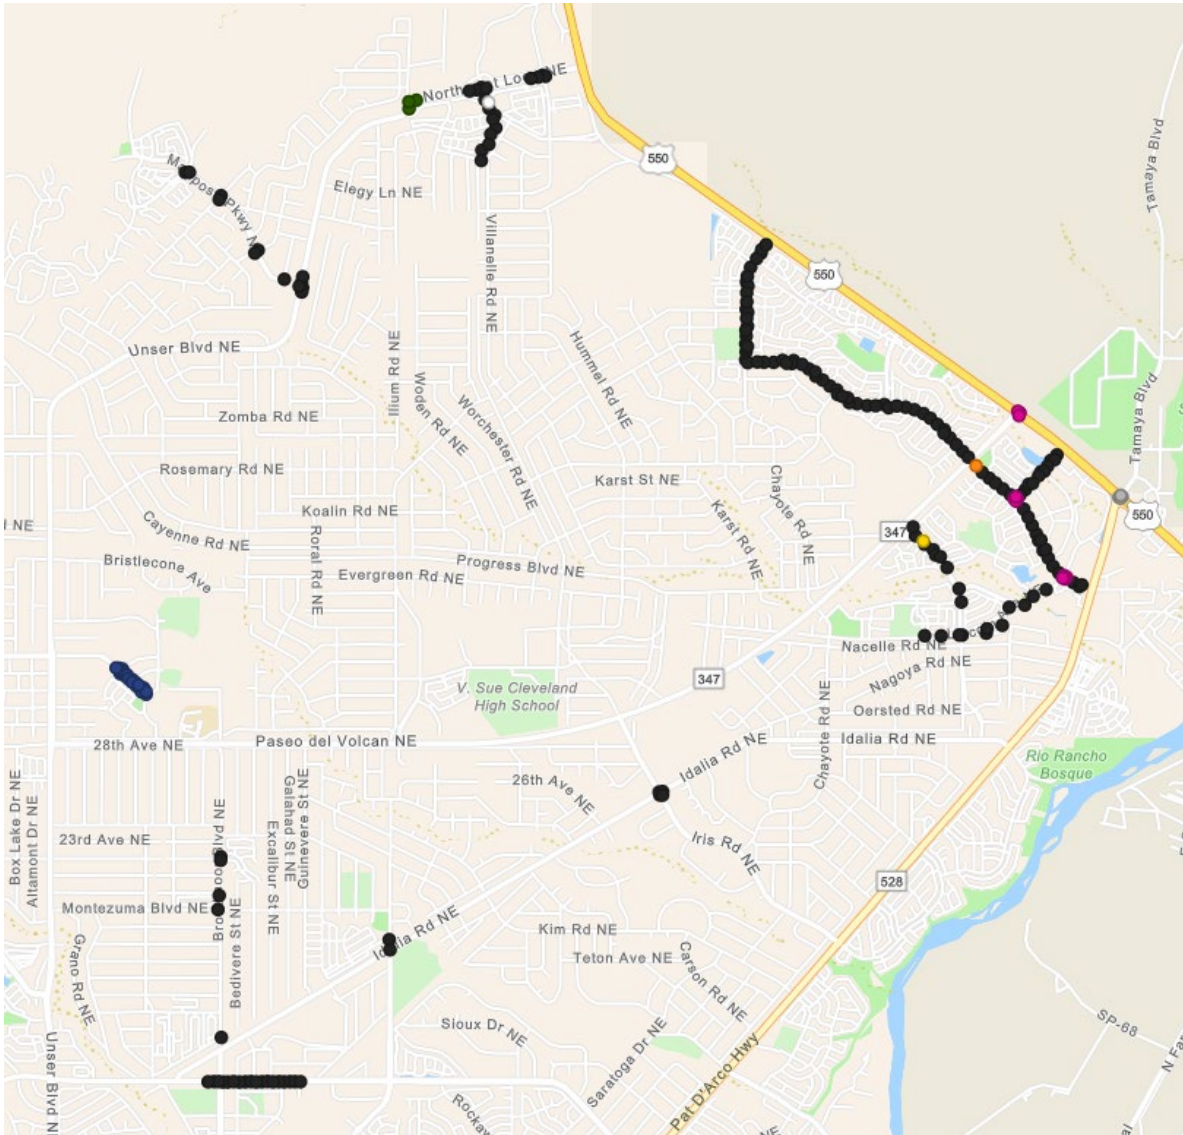


LEGEND

BLACK: Upgrade Complete
ALL OTHER COLORS: Scheduled for Upgrade

October 3, 2023

Segment Three Progress Map

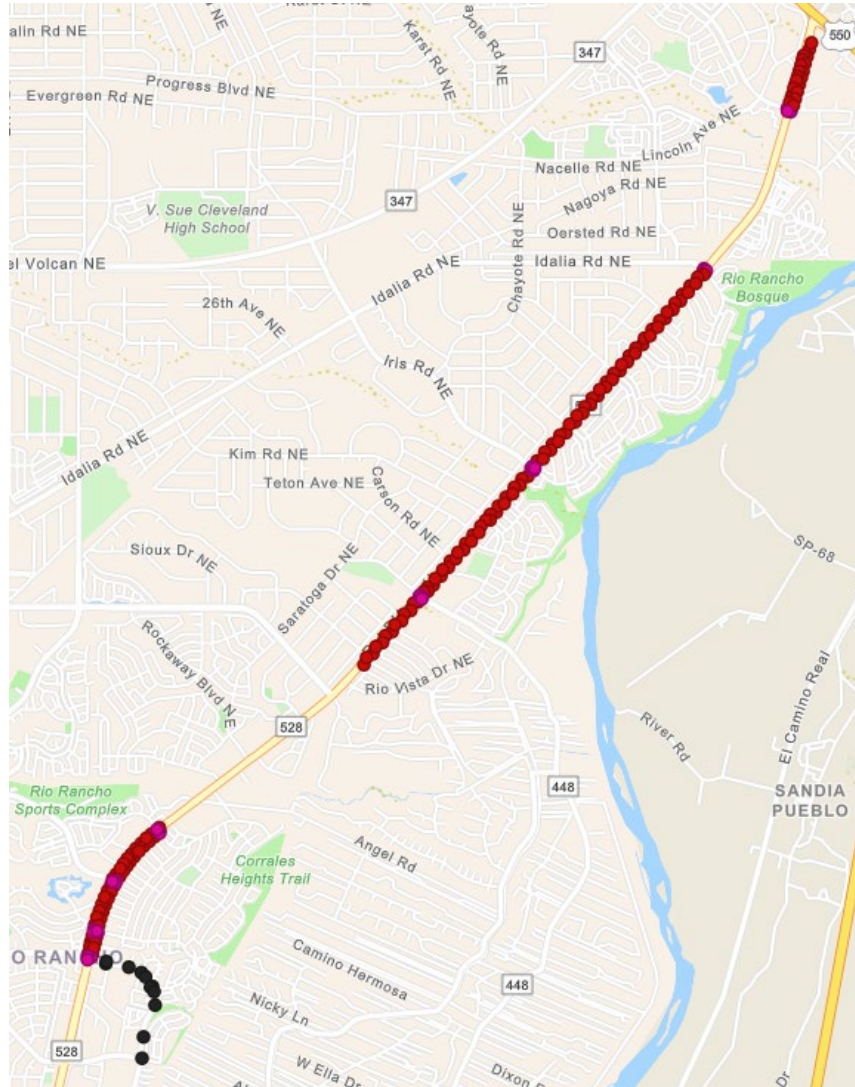


LEGEND

BLACK: Upgrade Complete
ALL OTHER COLORS: Scheduled for Upgrade

October 3, 2023

Segment Four Progress Map

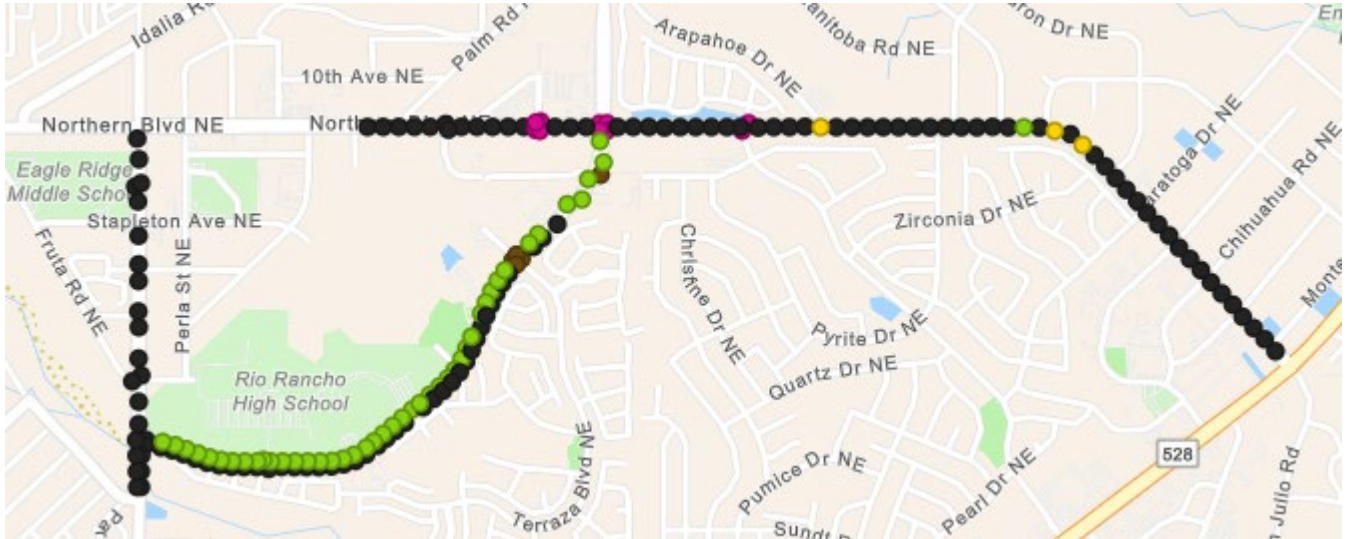


LEGEND

BLACK: Upgrade Complete
ALL OTHER COLORS: Scheduled for Upgrade

October 3, 2023

Segment Five Progress Map

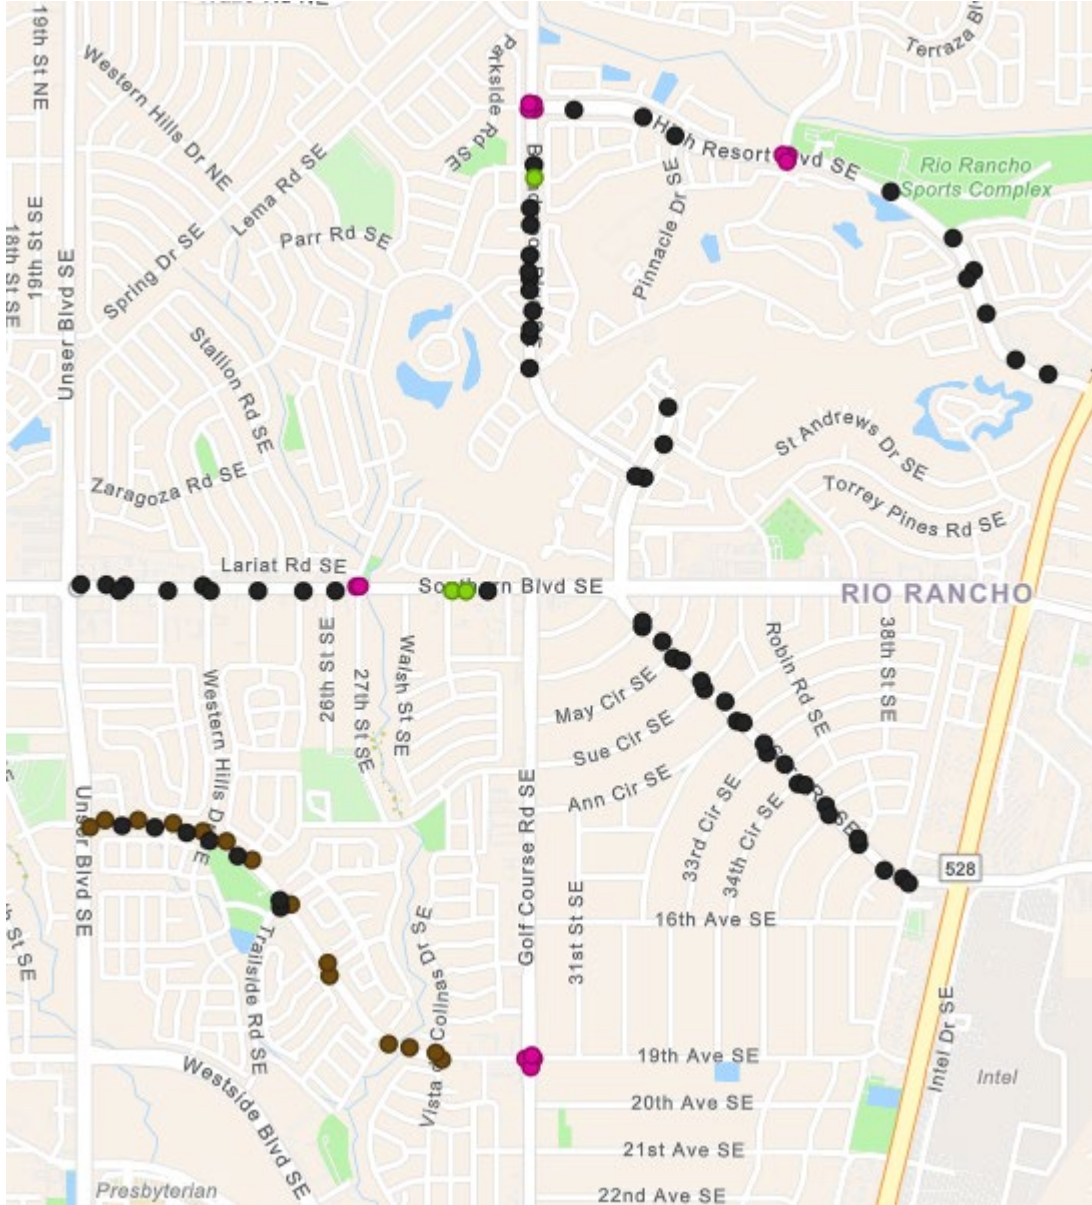

LEGEND

BLACK: Upgrade Complete
ALL OTHER COLORS: Scheduled for Upgrade
