



October 30, 2023

Project Status Overview

The Works Phase LED Conversion of City-owned arterial roadway streetlights installation continued the past two weeks spanning Monday, 10/16/23, to Friday, 10/27/23. In this two-week period, 115 luminaires were installed.

In total, 1085 luminaires have been installed which is 90% of the project scope.

The past two weeks, Dalkia continued work in Segment Three along NM528. A total of 155 luminaires have been installed in Segment Three.

In Segment Five, Dalkia worked along Cabezon Blvd. A total of 81 luminaires have been installed in this segment.

Dalkia also continued work on traffic signal luminaires across multiple segments.

Twenty-four shields have been installed on converted lights, per constituent requests.

Looking ahead, Dalkia will continue to work in Segments One, Two, and Three to complete the traffic signal luminaires.

Conversion Work Completed from 08/21/23 - 10/27/23

PROGRESS TO DATE

Total Complete: 1085 luminaires (90% complete)

Segment 1 363 luminaires (92% complete) Segment 2 232 luminaires (87% complete) Segment 3 155 luminaires (82% complete) Segment 4 254 luminaires (99% complete) Segment 5 81 luminaires (84% complete)


The maps on the following pages show Segment level progress between August 21, 2023 and October 27, 2023.





October 30, 2023

Segment One Progress Map

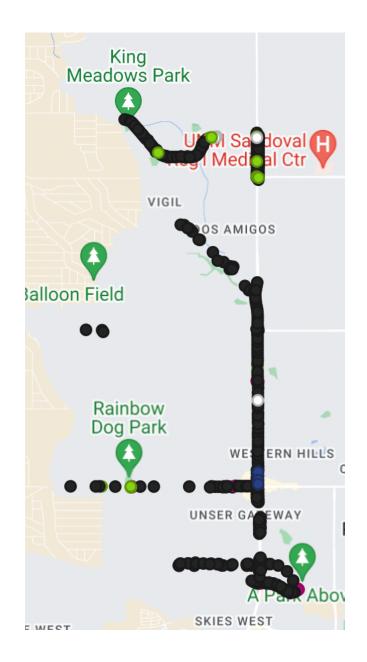

LEGEND

BLACK & LIGHT GREEN: Upgrade Complete ALL OTHER COLORS: Scheduled for Upgrade





October 30, 2023

Segment Two Progress Map



LEGEND


BLACK & LIGHT GREEN: Upgrade Complete ALL OTHER COLORS: Scheduled for Upgrade





October 30, 2023

Segment Three Progress Map

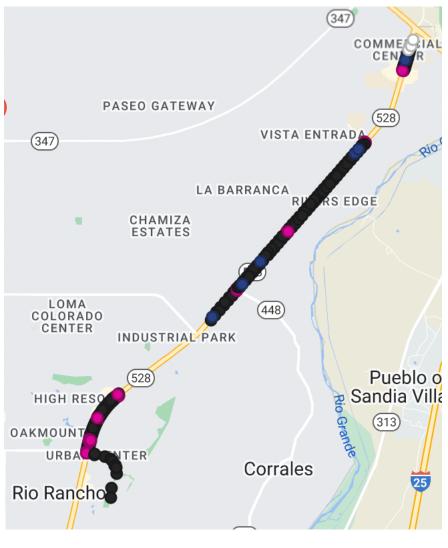

LEGEND


BLACK & LIGHT GREEN: Upgrade Complete ALL OTHER COLORS: Scheduled for Upgrade





October 30, 2023

Segment Four Progress Map

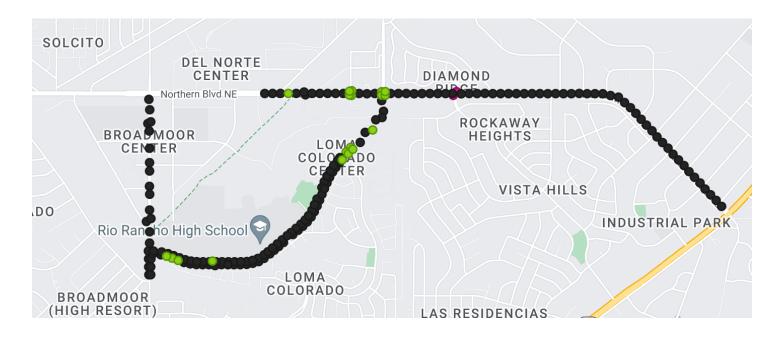

LEGEND


BLACK & LIGHT GREEN: Upgrade Complete ALL OTHER COLORS: Scheduled for Upgrade





October 30, 2023

Segment Five Progress Map

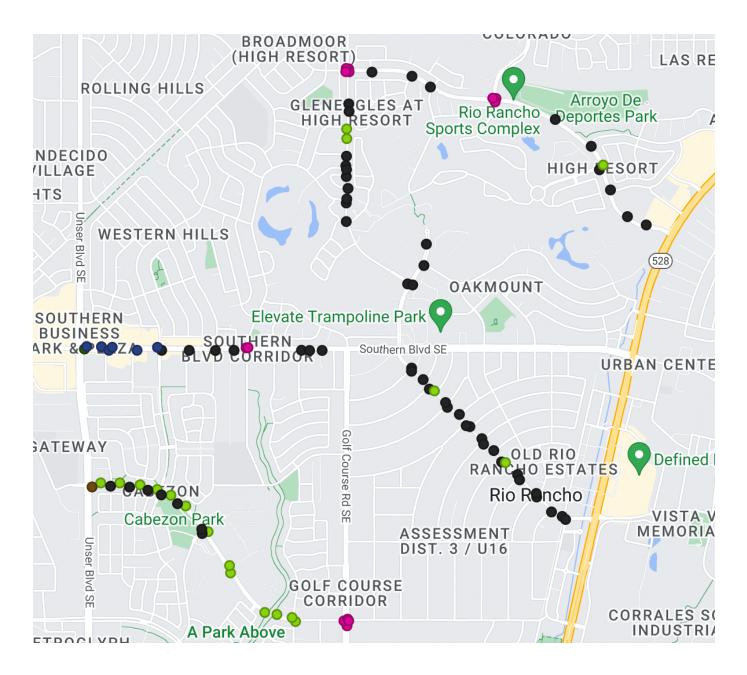

LEGEND

BLACK: Upgrade Complete ALL OTHER COLORS: Scheduled for Upgrade
