

September 6, 2023

Project Status Overview

The Works Phase LED Conversion of City-owned arterial roadway streetlights began installation on Monday, 08/21/23. In the first two weeks of construction, 329 luminaires were installed which is 26% of the total project scope.

The field crews began work in Segment One along King Blvd, Unser Blvd, Cherry Rd, Westside Blvd, and Wellspring Ave. A total of 212 luminaires were installed in Segment One.

In Segment Two, field crews performed work along Westphalia Blvd, Chayote Rd, and Enchanted Hills Blvd. A total of 117 luminaires were installed in Segment Two.

Looking ahead, Dalkia will continue installation in Segment One along Unser Blvd and Southern Blvd to bring this Segment to substantially complete, as well as continued work in Segment Two.

Conversion Work Completed from 08/21/23 – 09/01/23


PROGRESS TO DATE

Total Complete: 329 (26% complete)
Segment 1: 212 (53% complete)
Segment 2: 117 (44% complete)

The maps on the following pages show Segment level progress between August 21, 2023 and September 1, 2023.

September 6, 2023

Segment One Progress Map

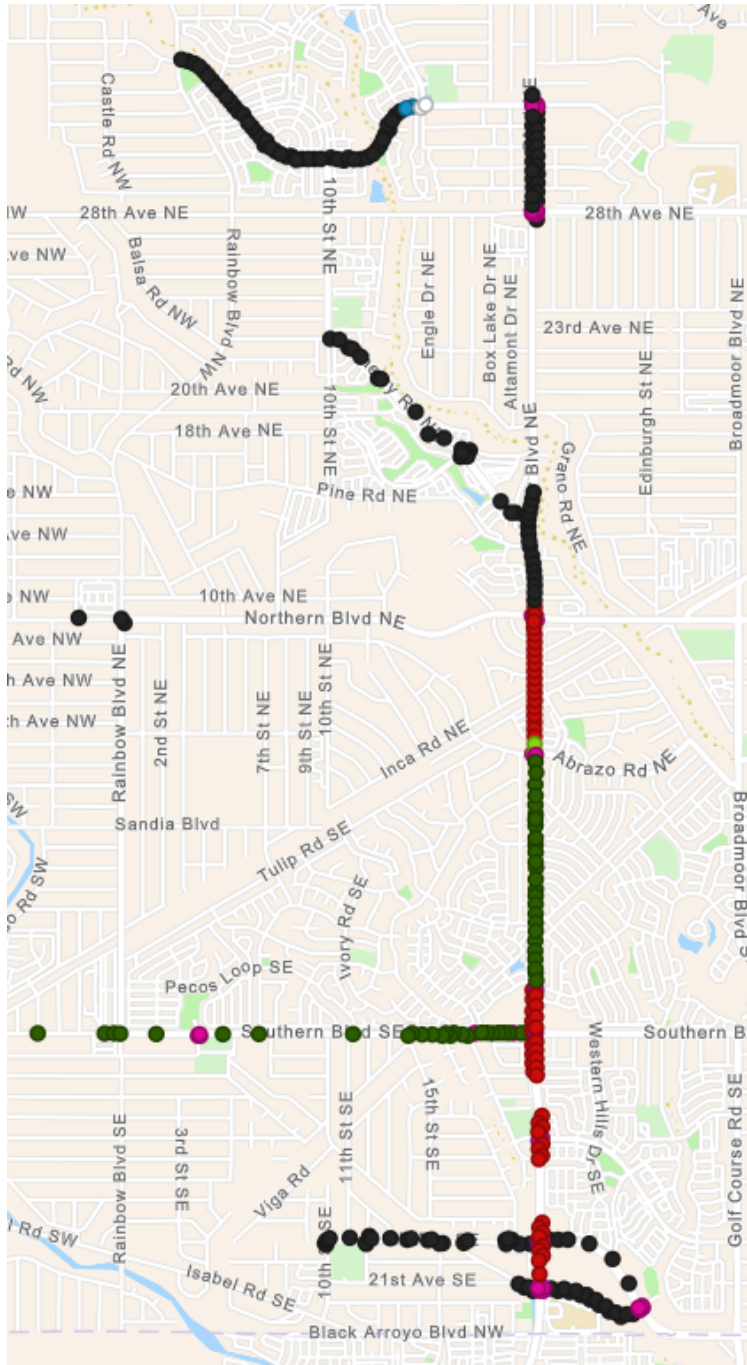


LEGEND

BLACK: Upgrade Complete
ALL OTHER COLORS: Scheduled for Upgrade

September 6, 2023

Segment Two Progress Map

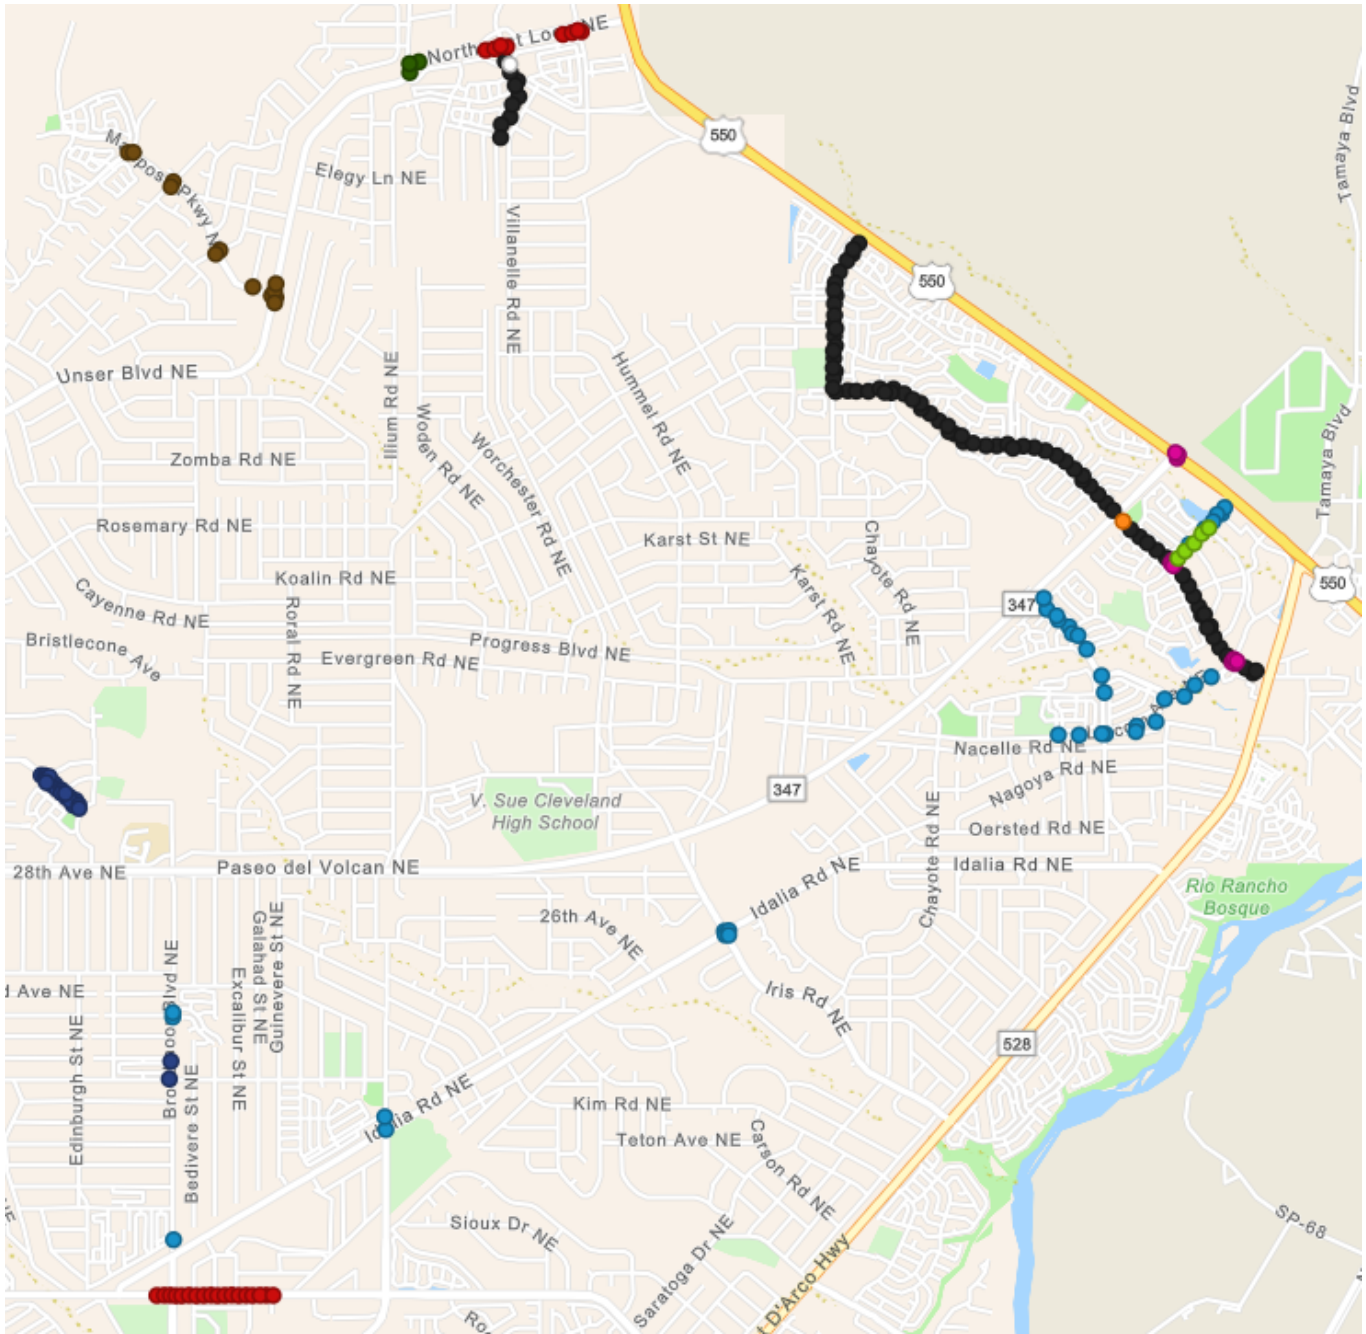

LEGEND

BLACK: Upgrade Complete
ALL OTHER COLORS: Scheduled for Upgrade
